

Application No. 18-04-____
Exhibit PAC/606
Witness: Timothy J. Hemstreet


BEFORE THE PUBLIC UTILITIES COMMISSION
OF THE STATE OF CALIFORNIA

PACIFICORP

Direct Testimony of Timothy J. Hemstreet

Wind Repowering Project Schedule

April 2018

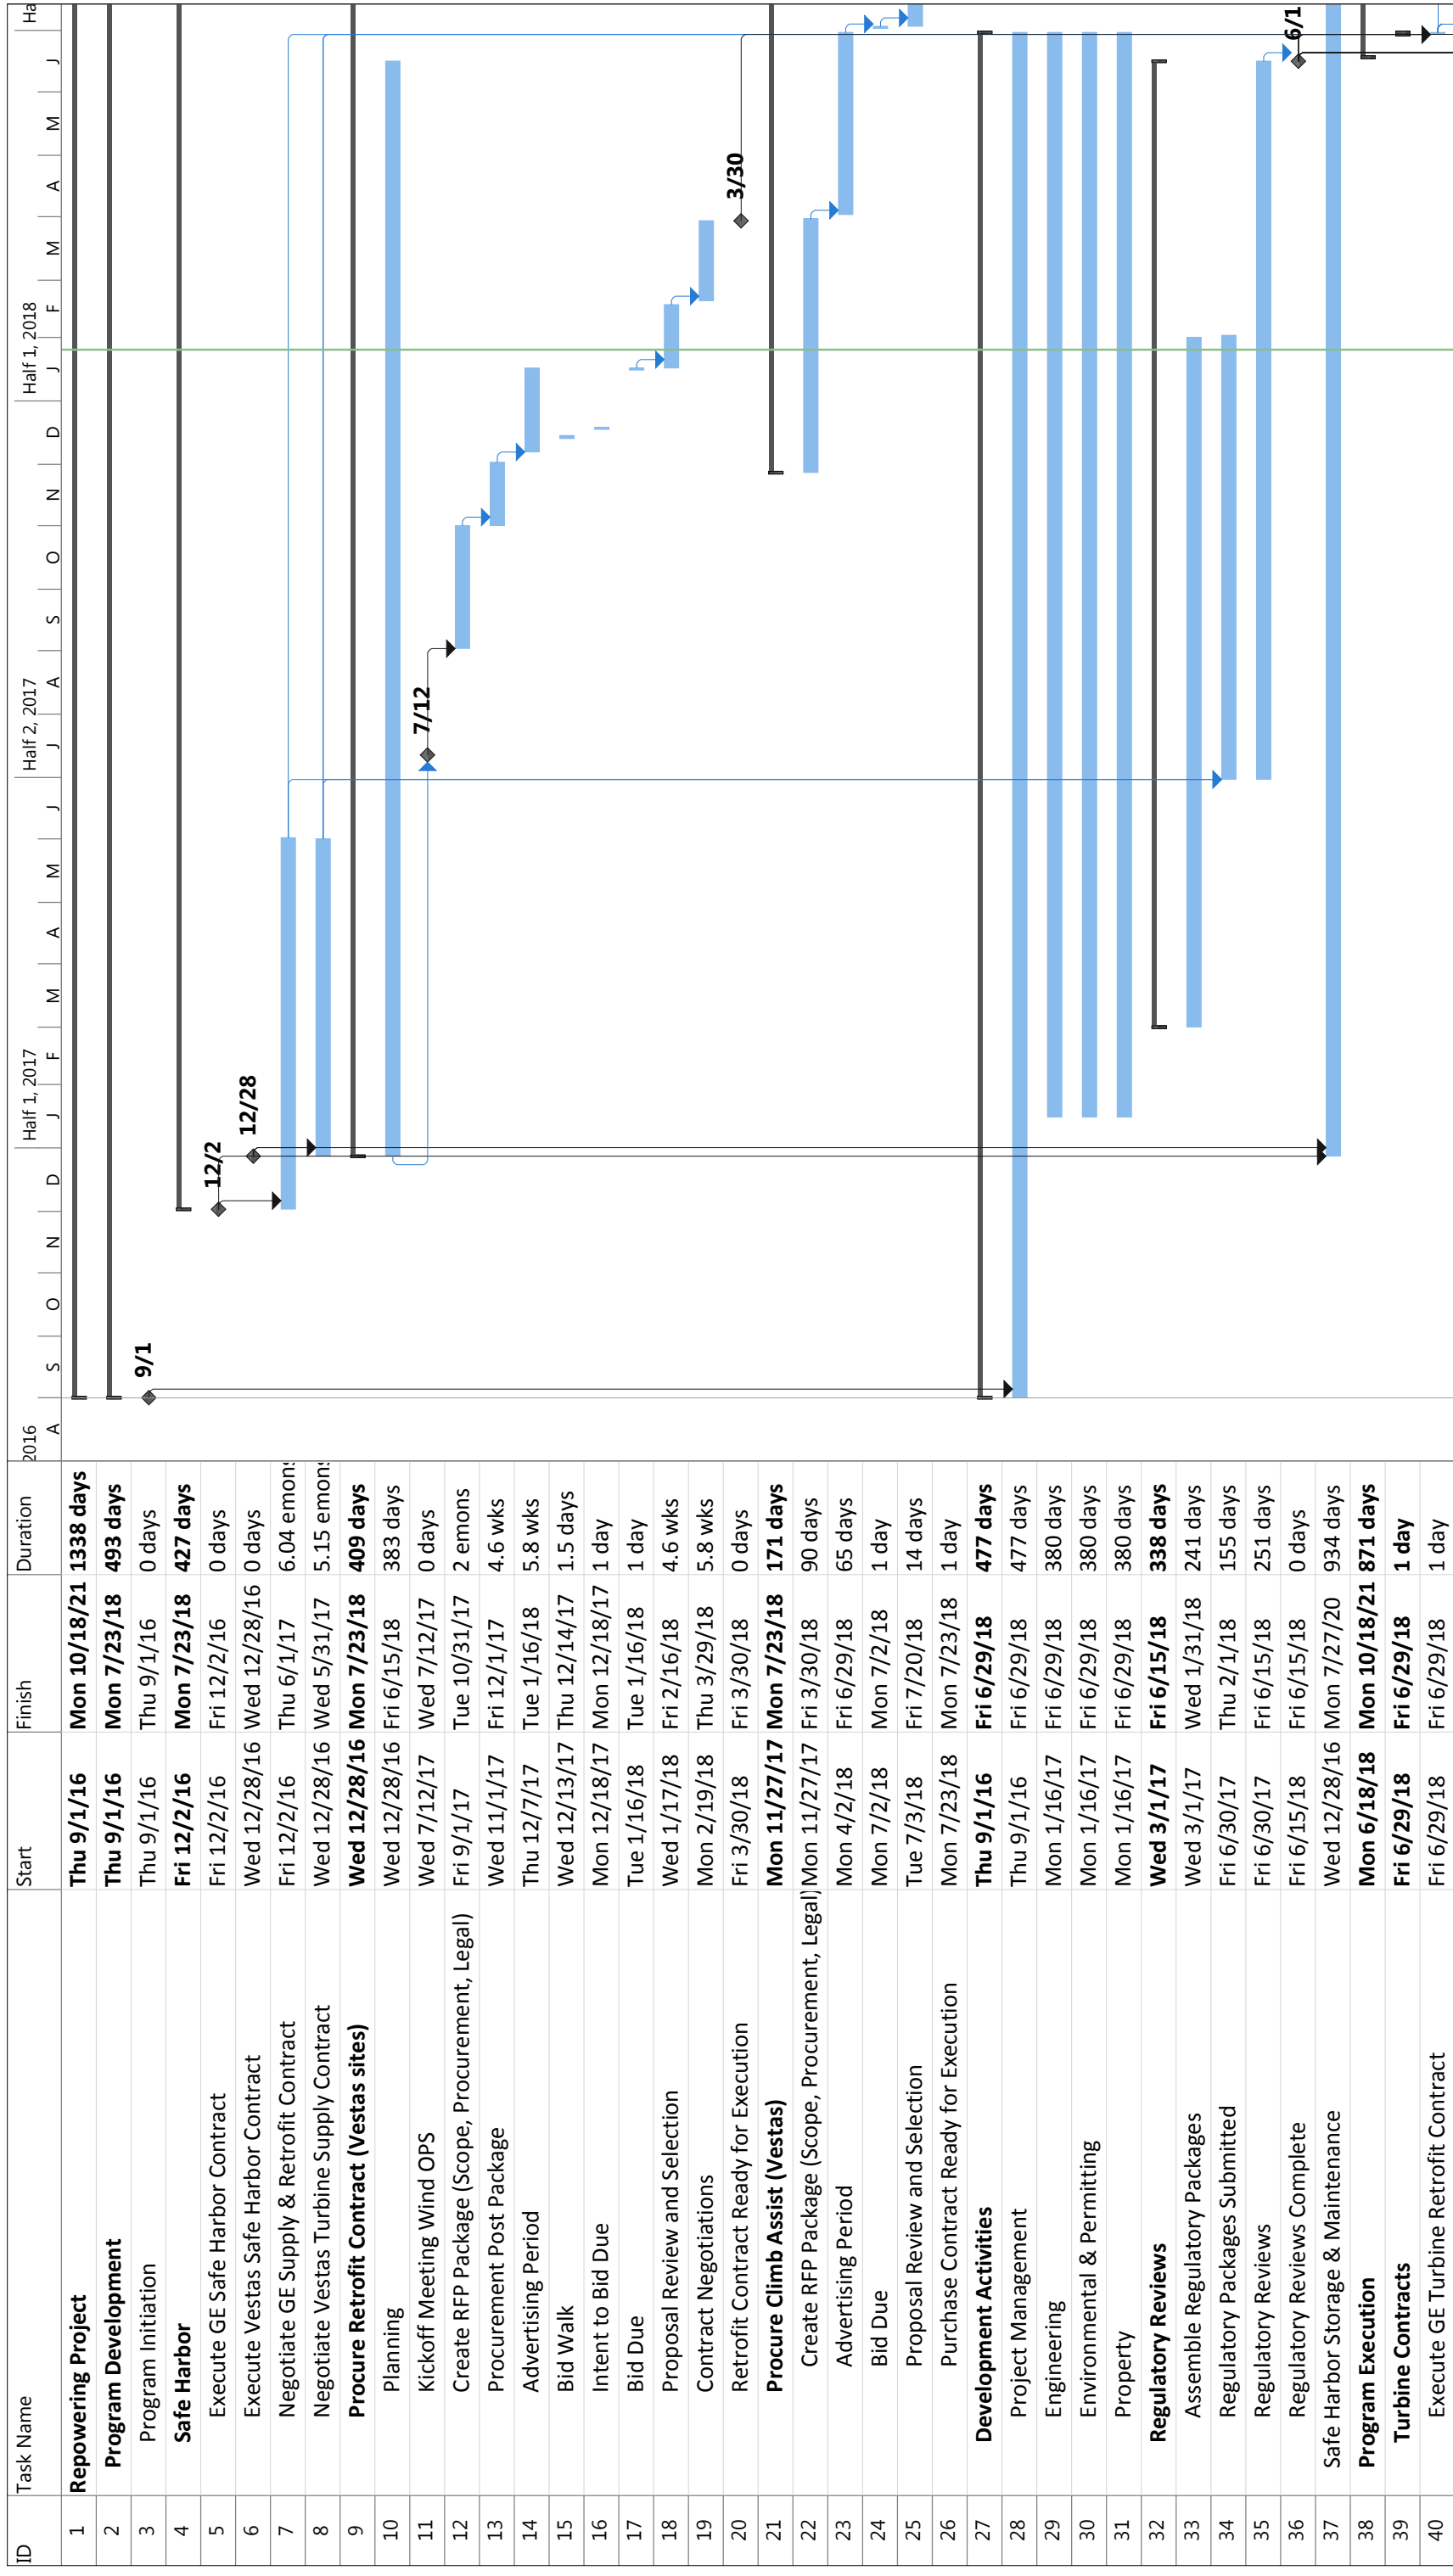

Project: Repower Schedule
Date: Fri 1/26/18

Task

Split

Milestone

Summary

Project Summary

ID	Task Name	Start	Finish	Duration	2016	A	S	O	N	D	Half 1, 2017	Half 2, 2017	A	M	J	F	S	O	N	D	Half 1, 2018	Half 2, 2018	A	M	J	Ha		
41	Execute Vestas Turbine Retrofit Contract	Fri 6/29/18	Fri 6/29/18	1 day																								
42	Execute Retrofit Contract (Vestas sites)	Fri 6/29/18	Fri 6/29/18	1 day																								
43	Management	Mon 6/18/18	Mon 10/18/21	871 days																								
44	Project Management	Mon 6/18/18	Mon 10/18/21	871 days																								
45	Engineering	Mon 6/18/18	Wed 4/21/21	743 days																								
46	Environmental & Permitting	Mon 6/18/18	Wed 4/21/21	743 days																								
47	Property	Mon 6/18/18	Thu 12/17/20	654 days																								
48	Construction Management	Mon 6/18/18	Mon 10/18/21	871 days																								
49	Project Execution	Fri 6/29/18	Mon 5/31/21	761 days																								
50	WTG Installation Periods	Fri 3/15/19	Tue 11/10/20	432 days																								
53	Glenrock Area	Fri 6/29/18	Sat 4/18/20	470 days																								
54	Glenrock I	Fri 6/29/18	Sat 4/18/20	470 days																								
55	Issue WTG Supply and Retrofit Contract Release	Fri 6/29/18	Fri 6/29/18	0 days																								
56	WTG Fabrication	Fri 6/29/18	Sun 2/24/19	8 emons																								
57	Site Civil Works / BOP	Mon 7/2/18	Fri 9/27/19	325 days																								
58	Transport and Delivery	Mon 2/25/19	Fri 9/6/19	28 wks																								
59	WTG Installation	Mon 3/18/19	Fri 9/27/19	28 wks																								
60	Substantial Completion	Tue 10/1/19	Tue 10/1/19	0 days																								
61	Final Completion	Mon 10/21/19	Mon 10/21/19	0 days																								
62	Project Closeout	Mon 10/21/19	Sat 4/18/20	6 emons																								
63	Glenrock III	Fri 6/29/18	Sat 4/18/20	470 days																								
64	Issue WTG Supply and Retrofit Contract Release	Fri 6/29/18	Fri 6/29/18	0 days																								
65	WTG Fabrication	Fri 6/29/18	Sun 2/24/19	8 emons																								
66	Site Civil Works / BOP	Mon 7/2/18	Wed 10/30/19	348 days																								
67	Transport and Delivery	Mon 2/25/19	Fri 9/6/19	28 wks																								
68	WTG Installation	Mon 3/18/19	Fri 9/27/19	28 wks																								
69	Substantial Completion	Tue 10/1/19	Tue 10/1/19	0 days																								
70	Final Completion	Mon 10/21/19	Mon 10/21/19	0 days																								
71	Project Closeout	Mon 10/21/19	Sat 4/18/20	6 emons																								
72	Rolling Hills	Fri 6/29/18	Sat 4/18/20	470 days																								
73	Issue WTG Supply and Retrofit Contract Release	Fri 6/29/18	Fri 6/29/18	0 days																								
74	WTG Fabrication	Fri 6/29/18	Sun 2/24/19	8 emons																								
75	Site Civil Works / BOP	Mon 7/2/18	Wed 10/30/19	348 days																								
76	Transport and Delivery	Mon 2/25/19	Fri 9/6/19	28 wks																								
77	WTG Installation	Mon 3/18/19	Fri 9/27/19	28 wks																								
78	Substantial Completion	Tue 10/1/19	Tue 10/1/19	0 days																								
79	Final Completion	Mon 10/21/19	Mon 10/21/19	0 days																								
80	Project Closeout	Mon 10/21/19	Sat 4/18/20	6 emons																								
81	Seven Mile Hill Area	Fri 6/29/18	Wed 1/15/20	403 days																								
82	Seven Mile Hill I	Fri 6/29/18	Wed 1/15/20	403 days																								

Project: Repower Schedule
Date: Fri 1/26/18


Task Split Milestone


Summary Project Summary

ID	Task Name	Start	Finish	Duration	2016																	
					A	S	O	N	D	J	F	M	A	M	J	J	H					
163	WTG Installation	Fri 8/2/19	Thu 11/14/19	15 wks																		
164	Substantial Completion	Thu 11/14/19	Thu 11/14/19	0 days																		
165	Final Completion	Thu 12/5/19	Thu 12/5/19	0 days																		
166	Project Closeout	Thu 12/5/19	Tue 6/2/20	6 emons																		



Project: Repower Schedule Date: Fri 1/26/18	Task	Split	Milestone	Summary	Project Summary
--	------	-------	-----------	---------	-----------------

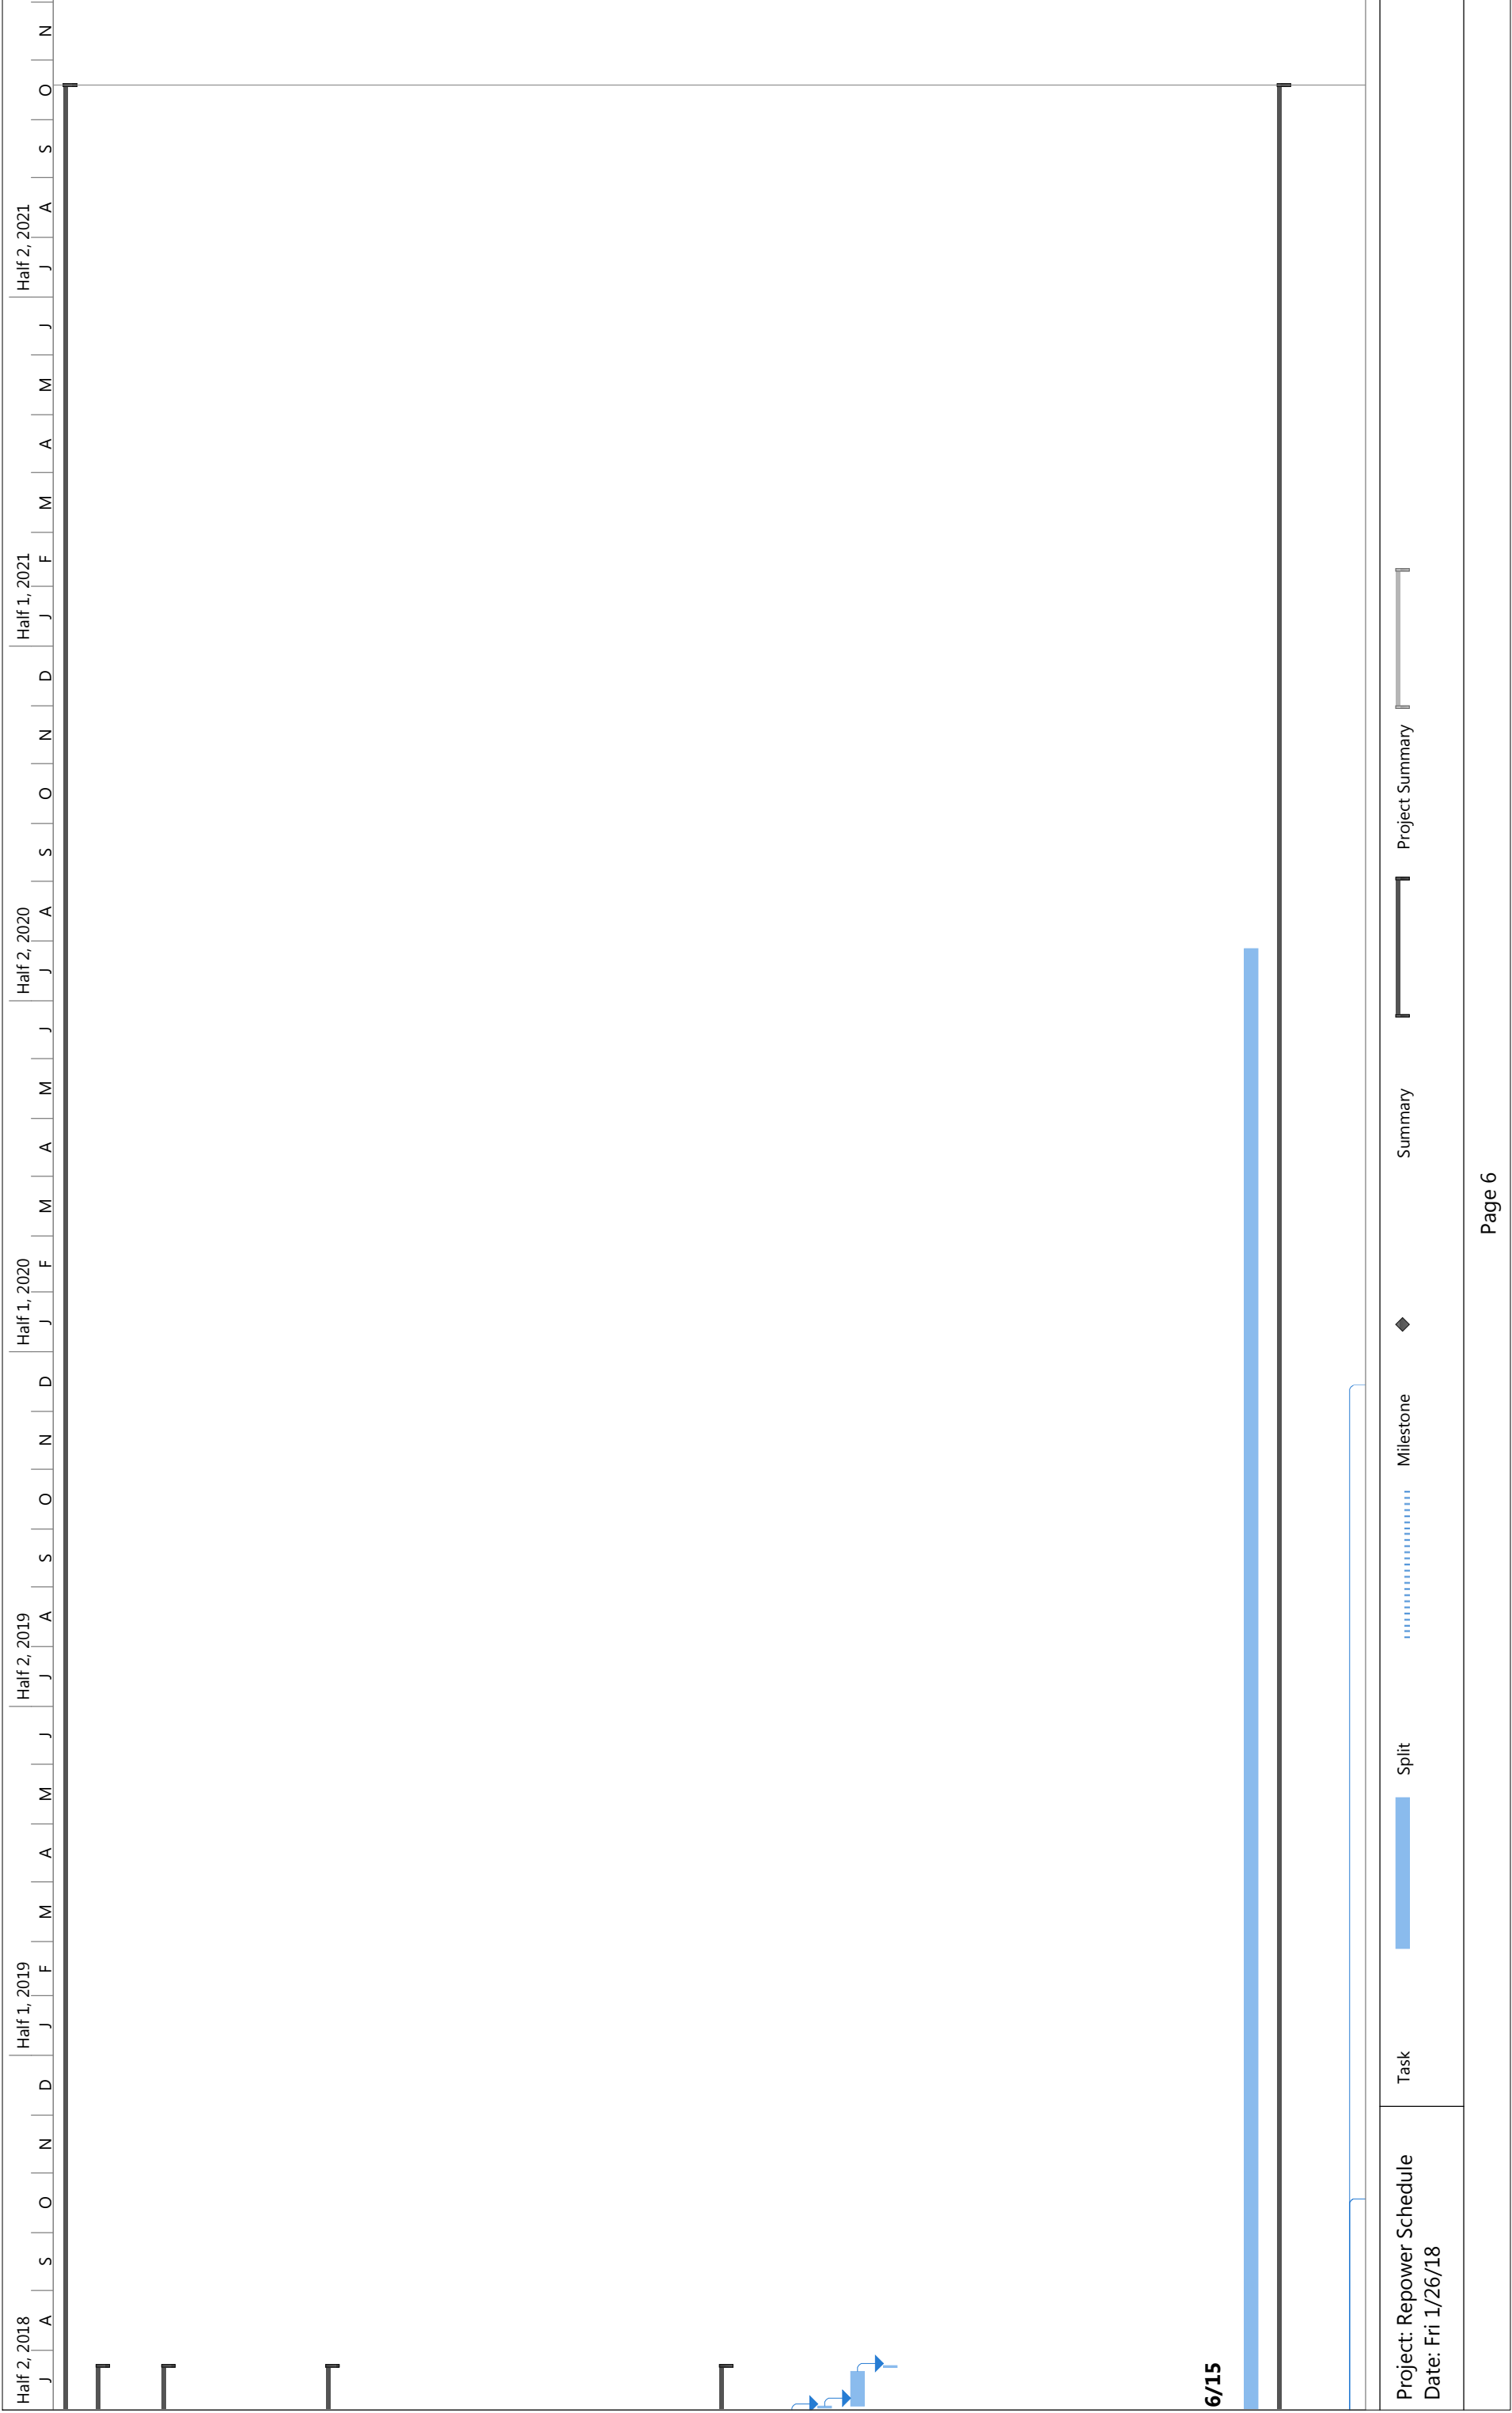

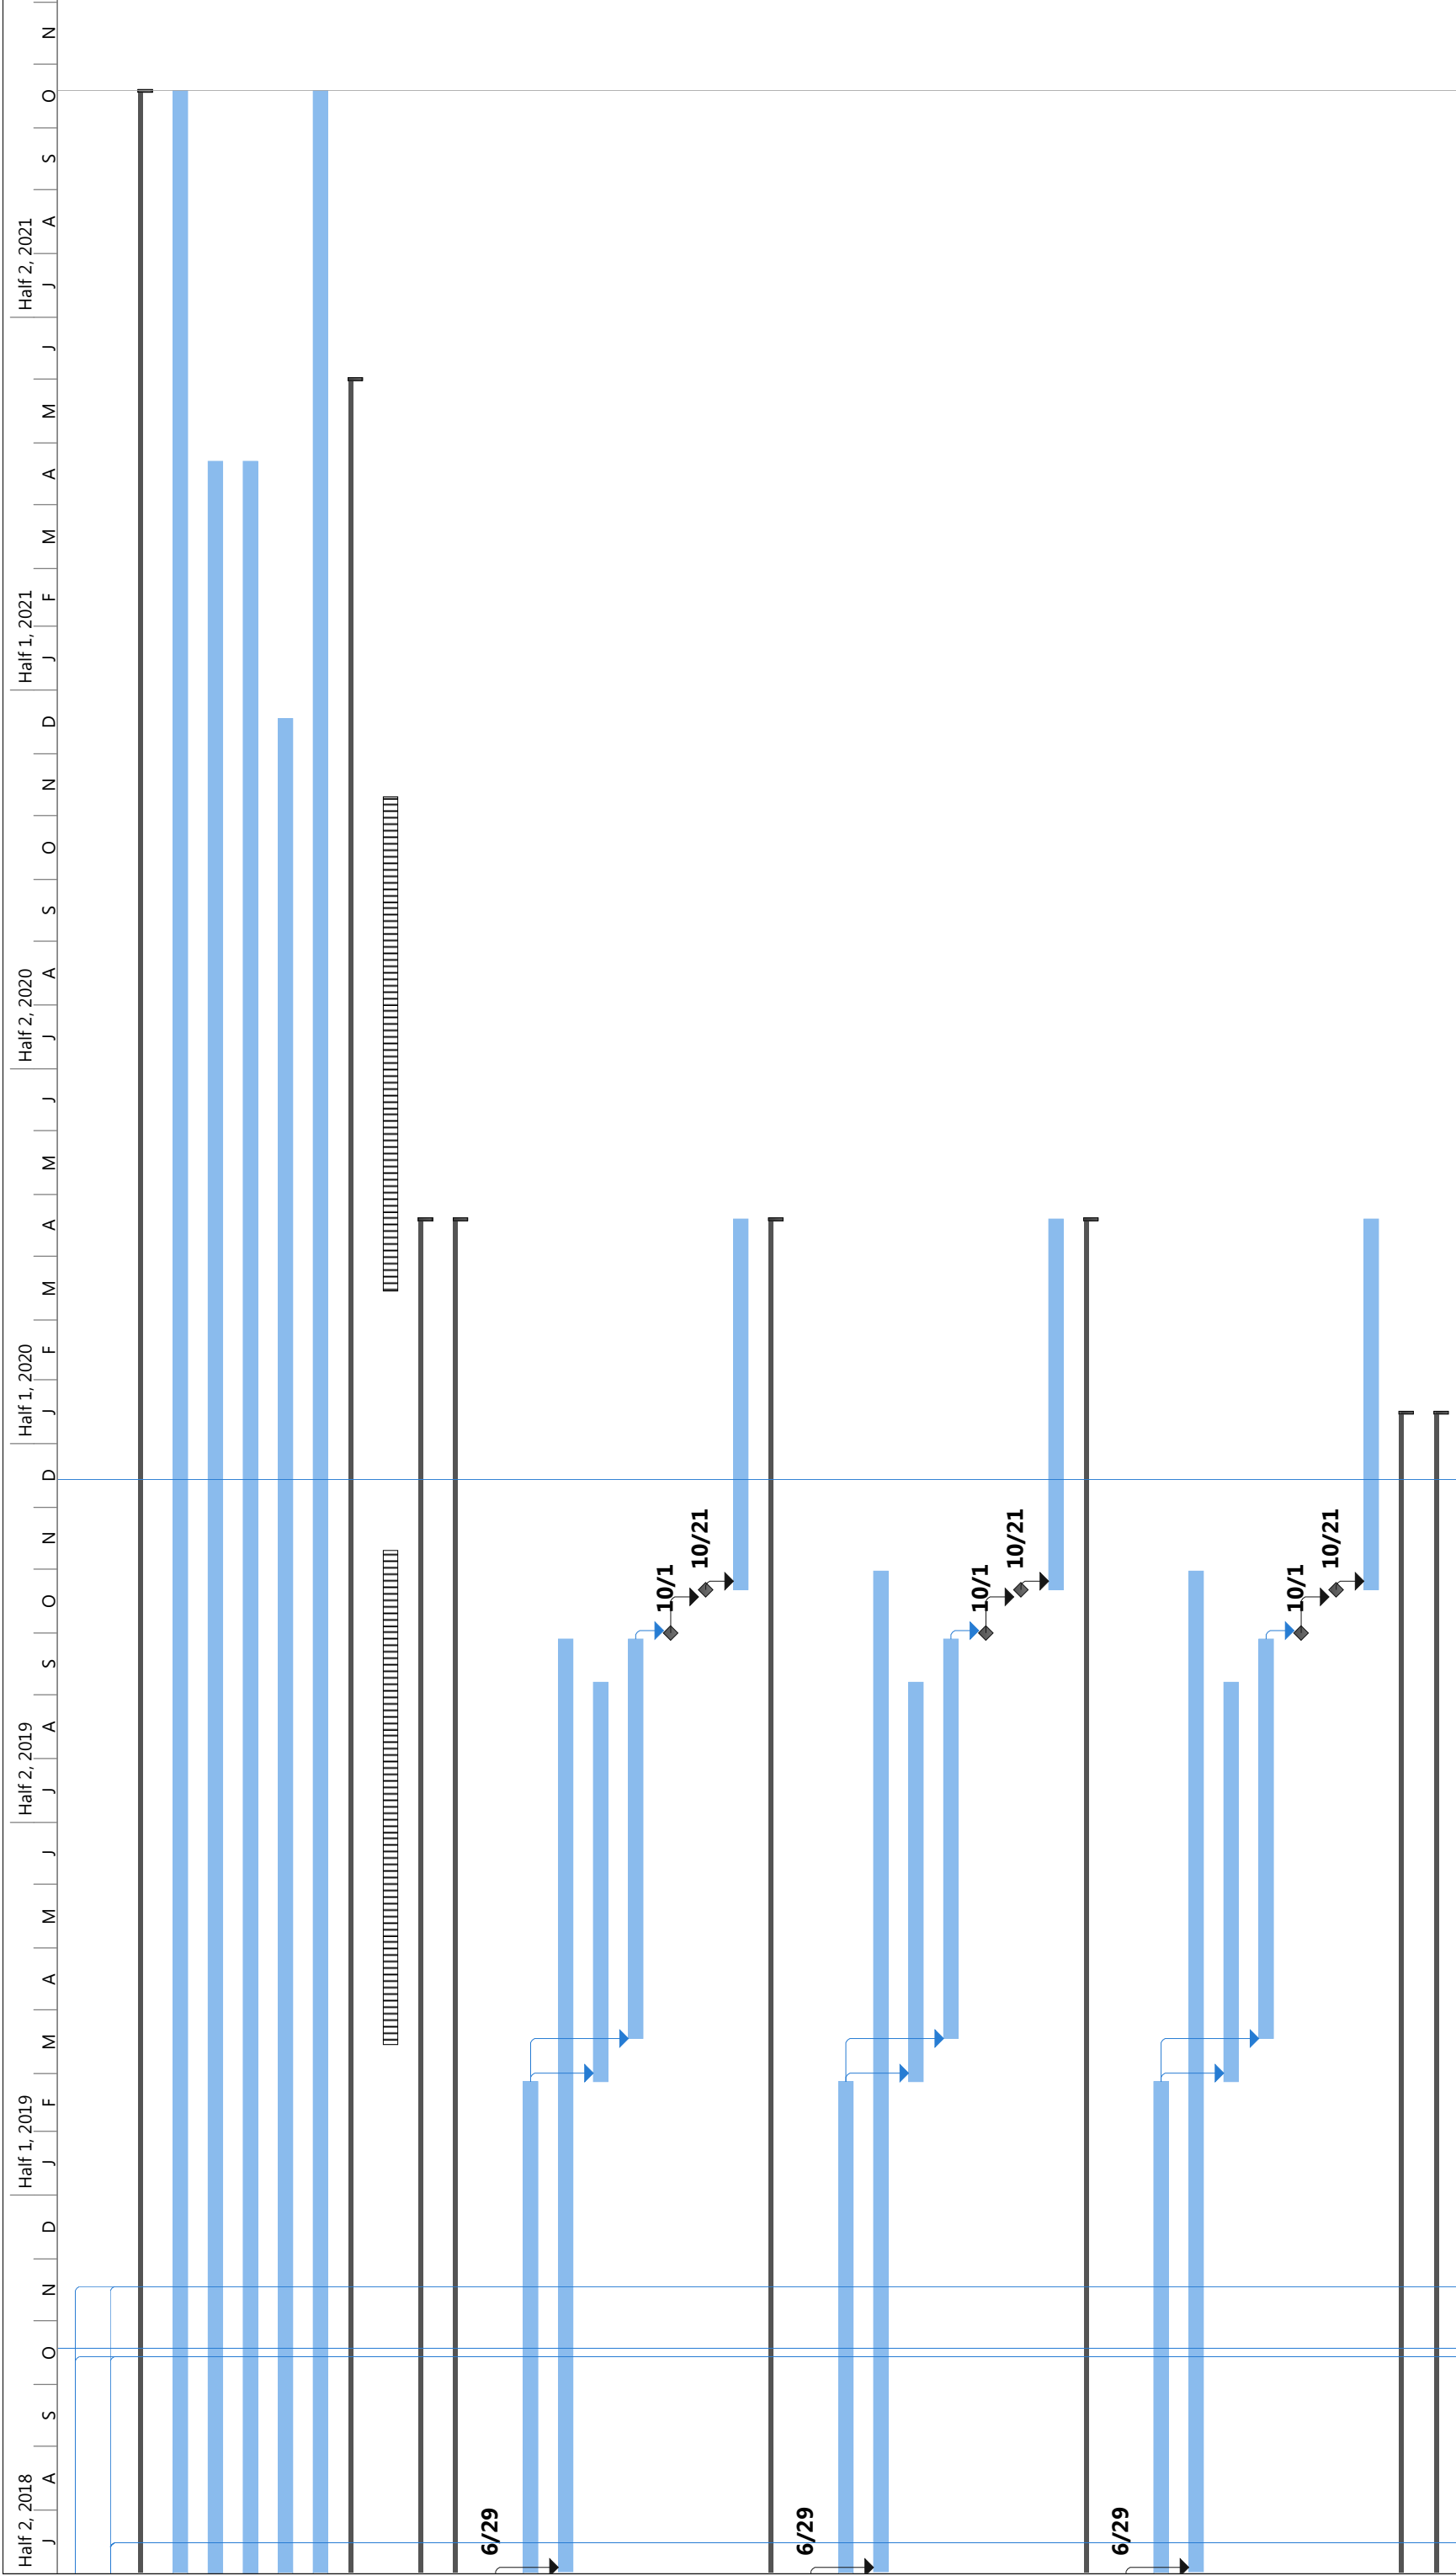

Project: Repower Schedule
 Date: Fri 1/26/18

Task


Split

Milestone

◆


Summary

Project Summary

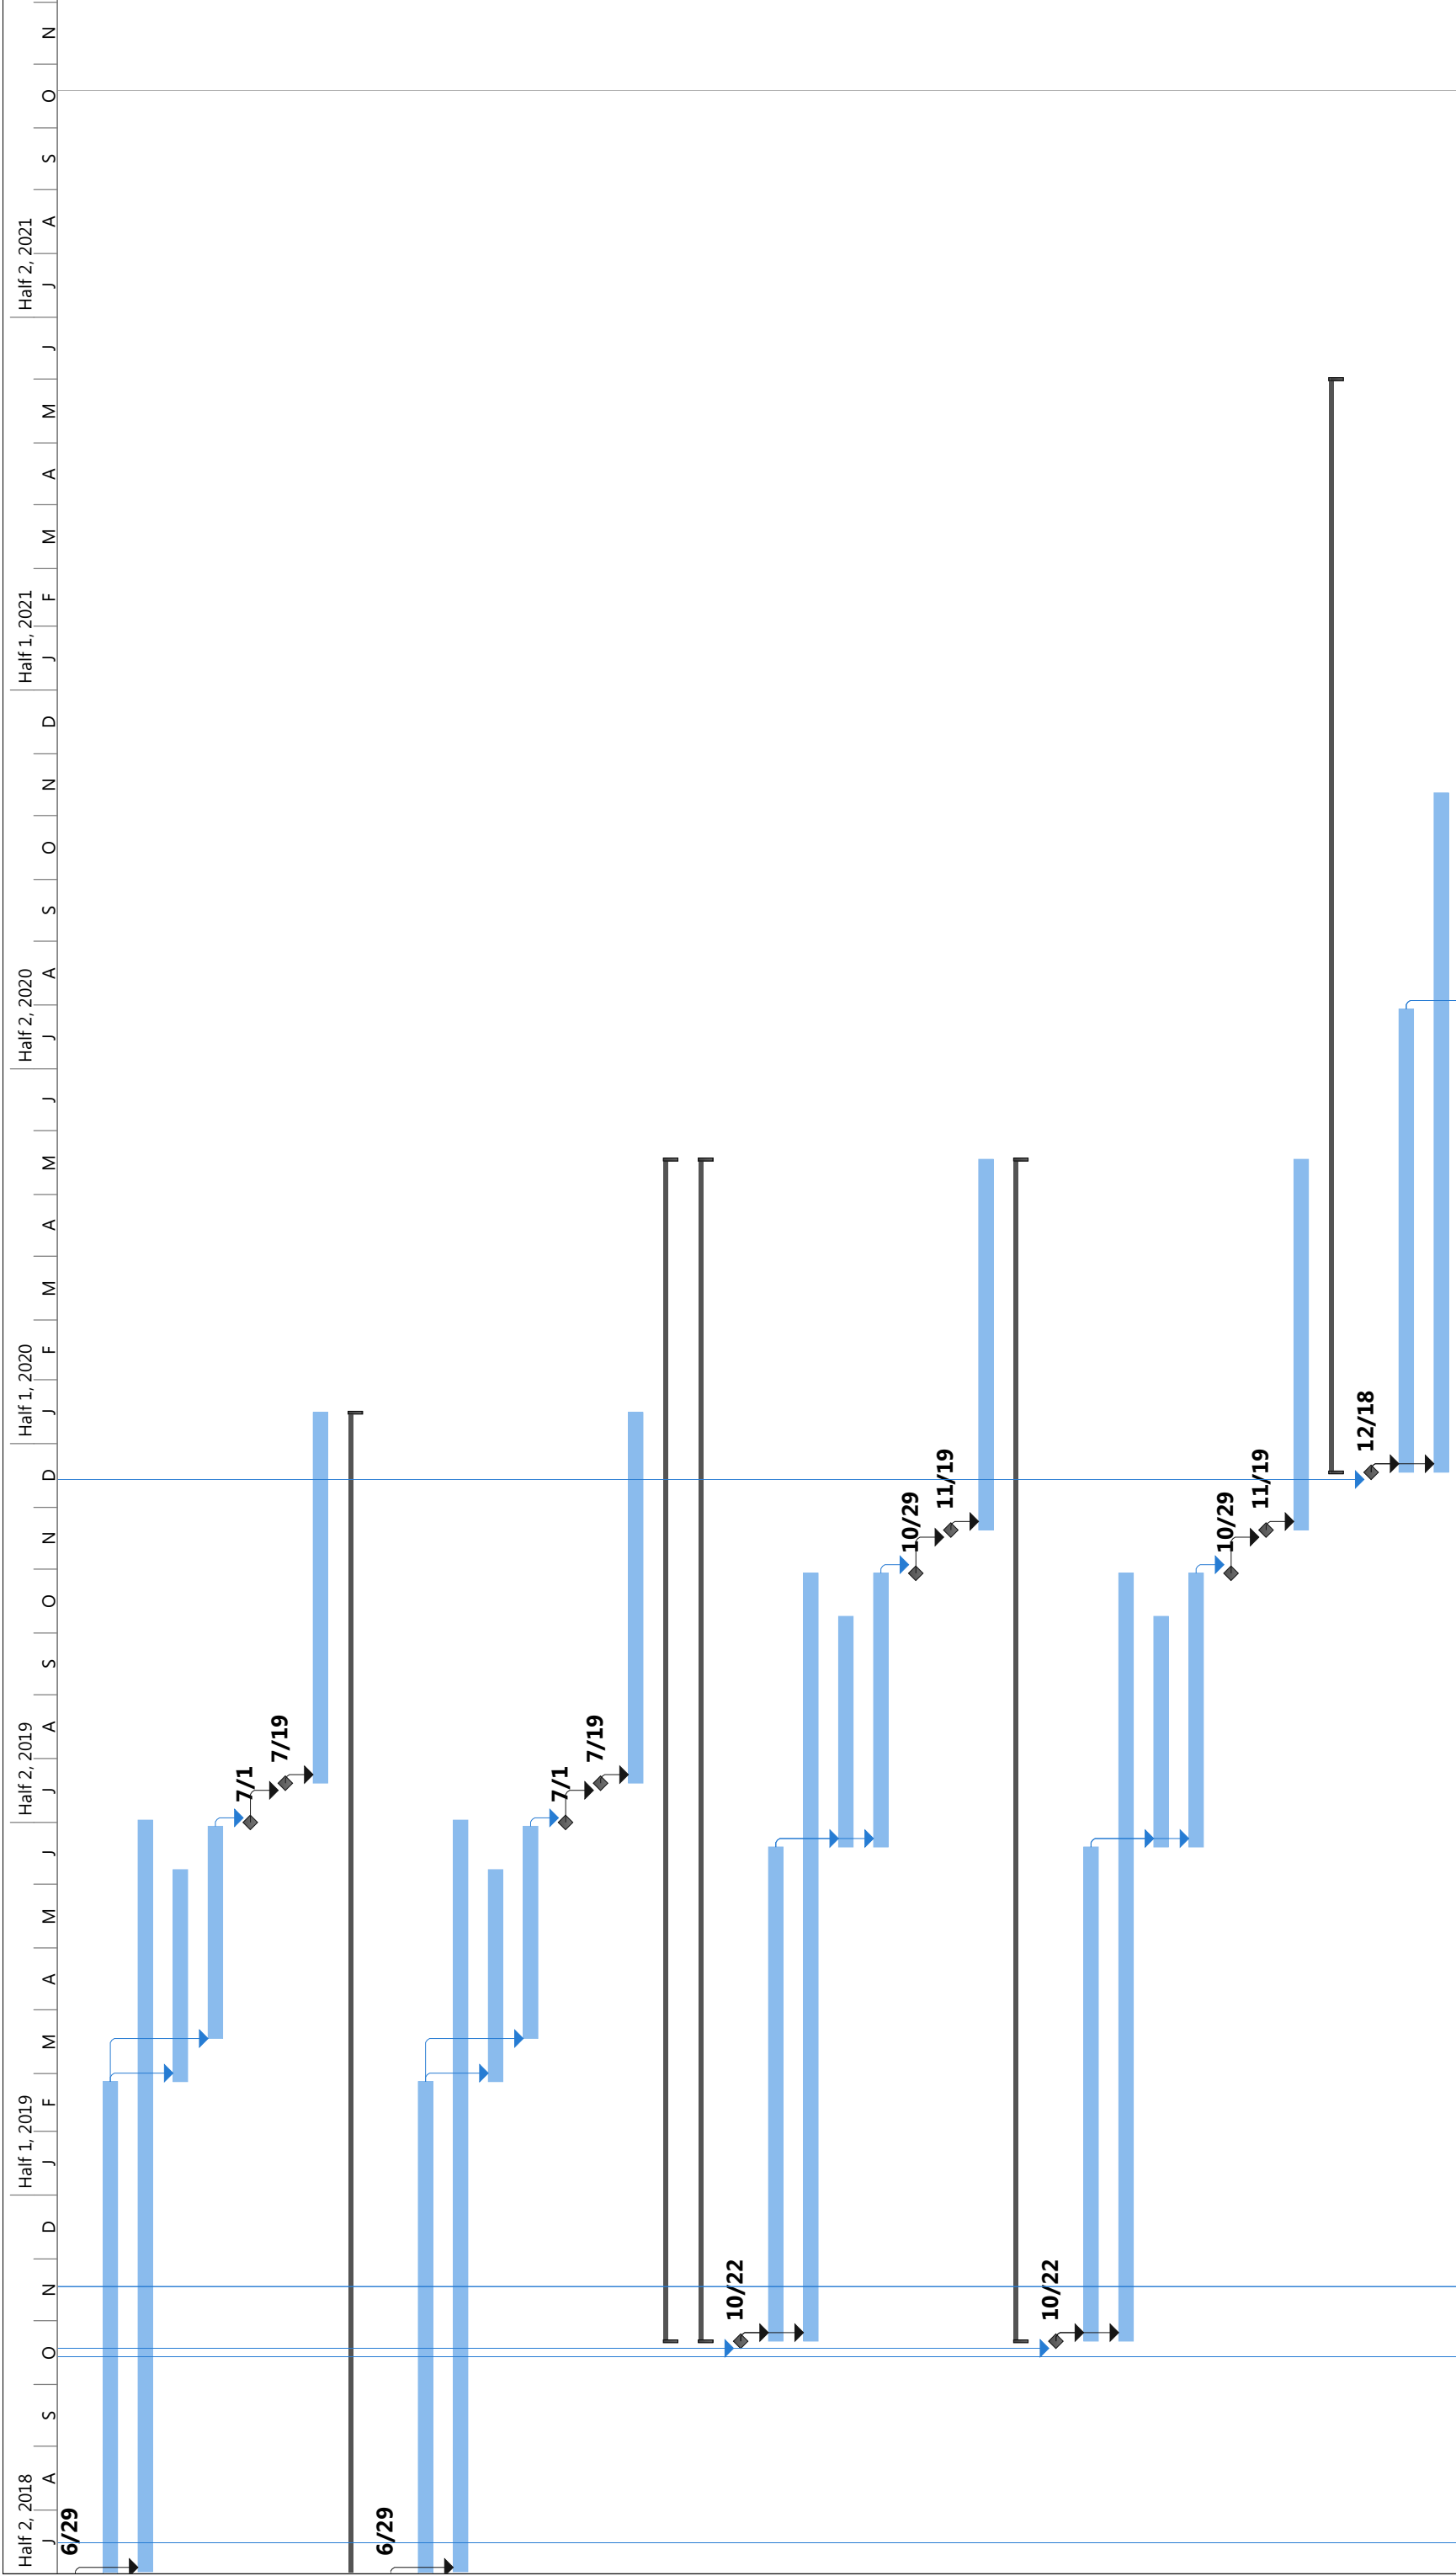

Project: Repower Schedule
 Date: Fri 1/26/18

Task
 Split
 Milestone
 Summary
 Project Summary

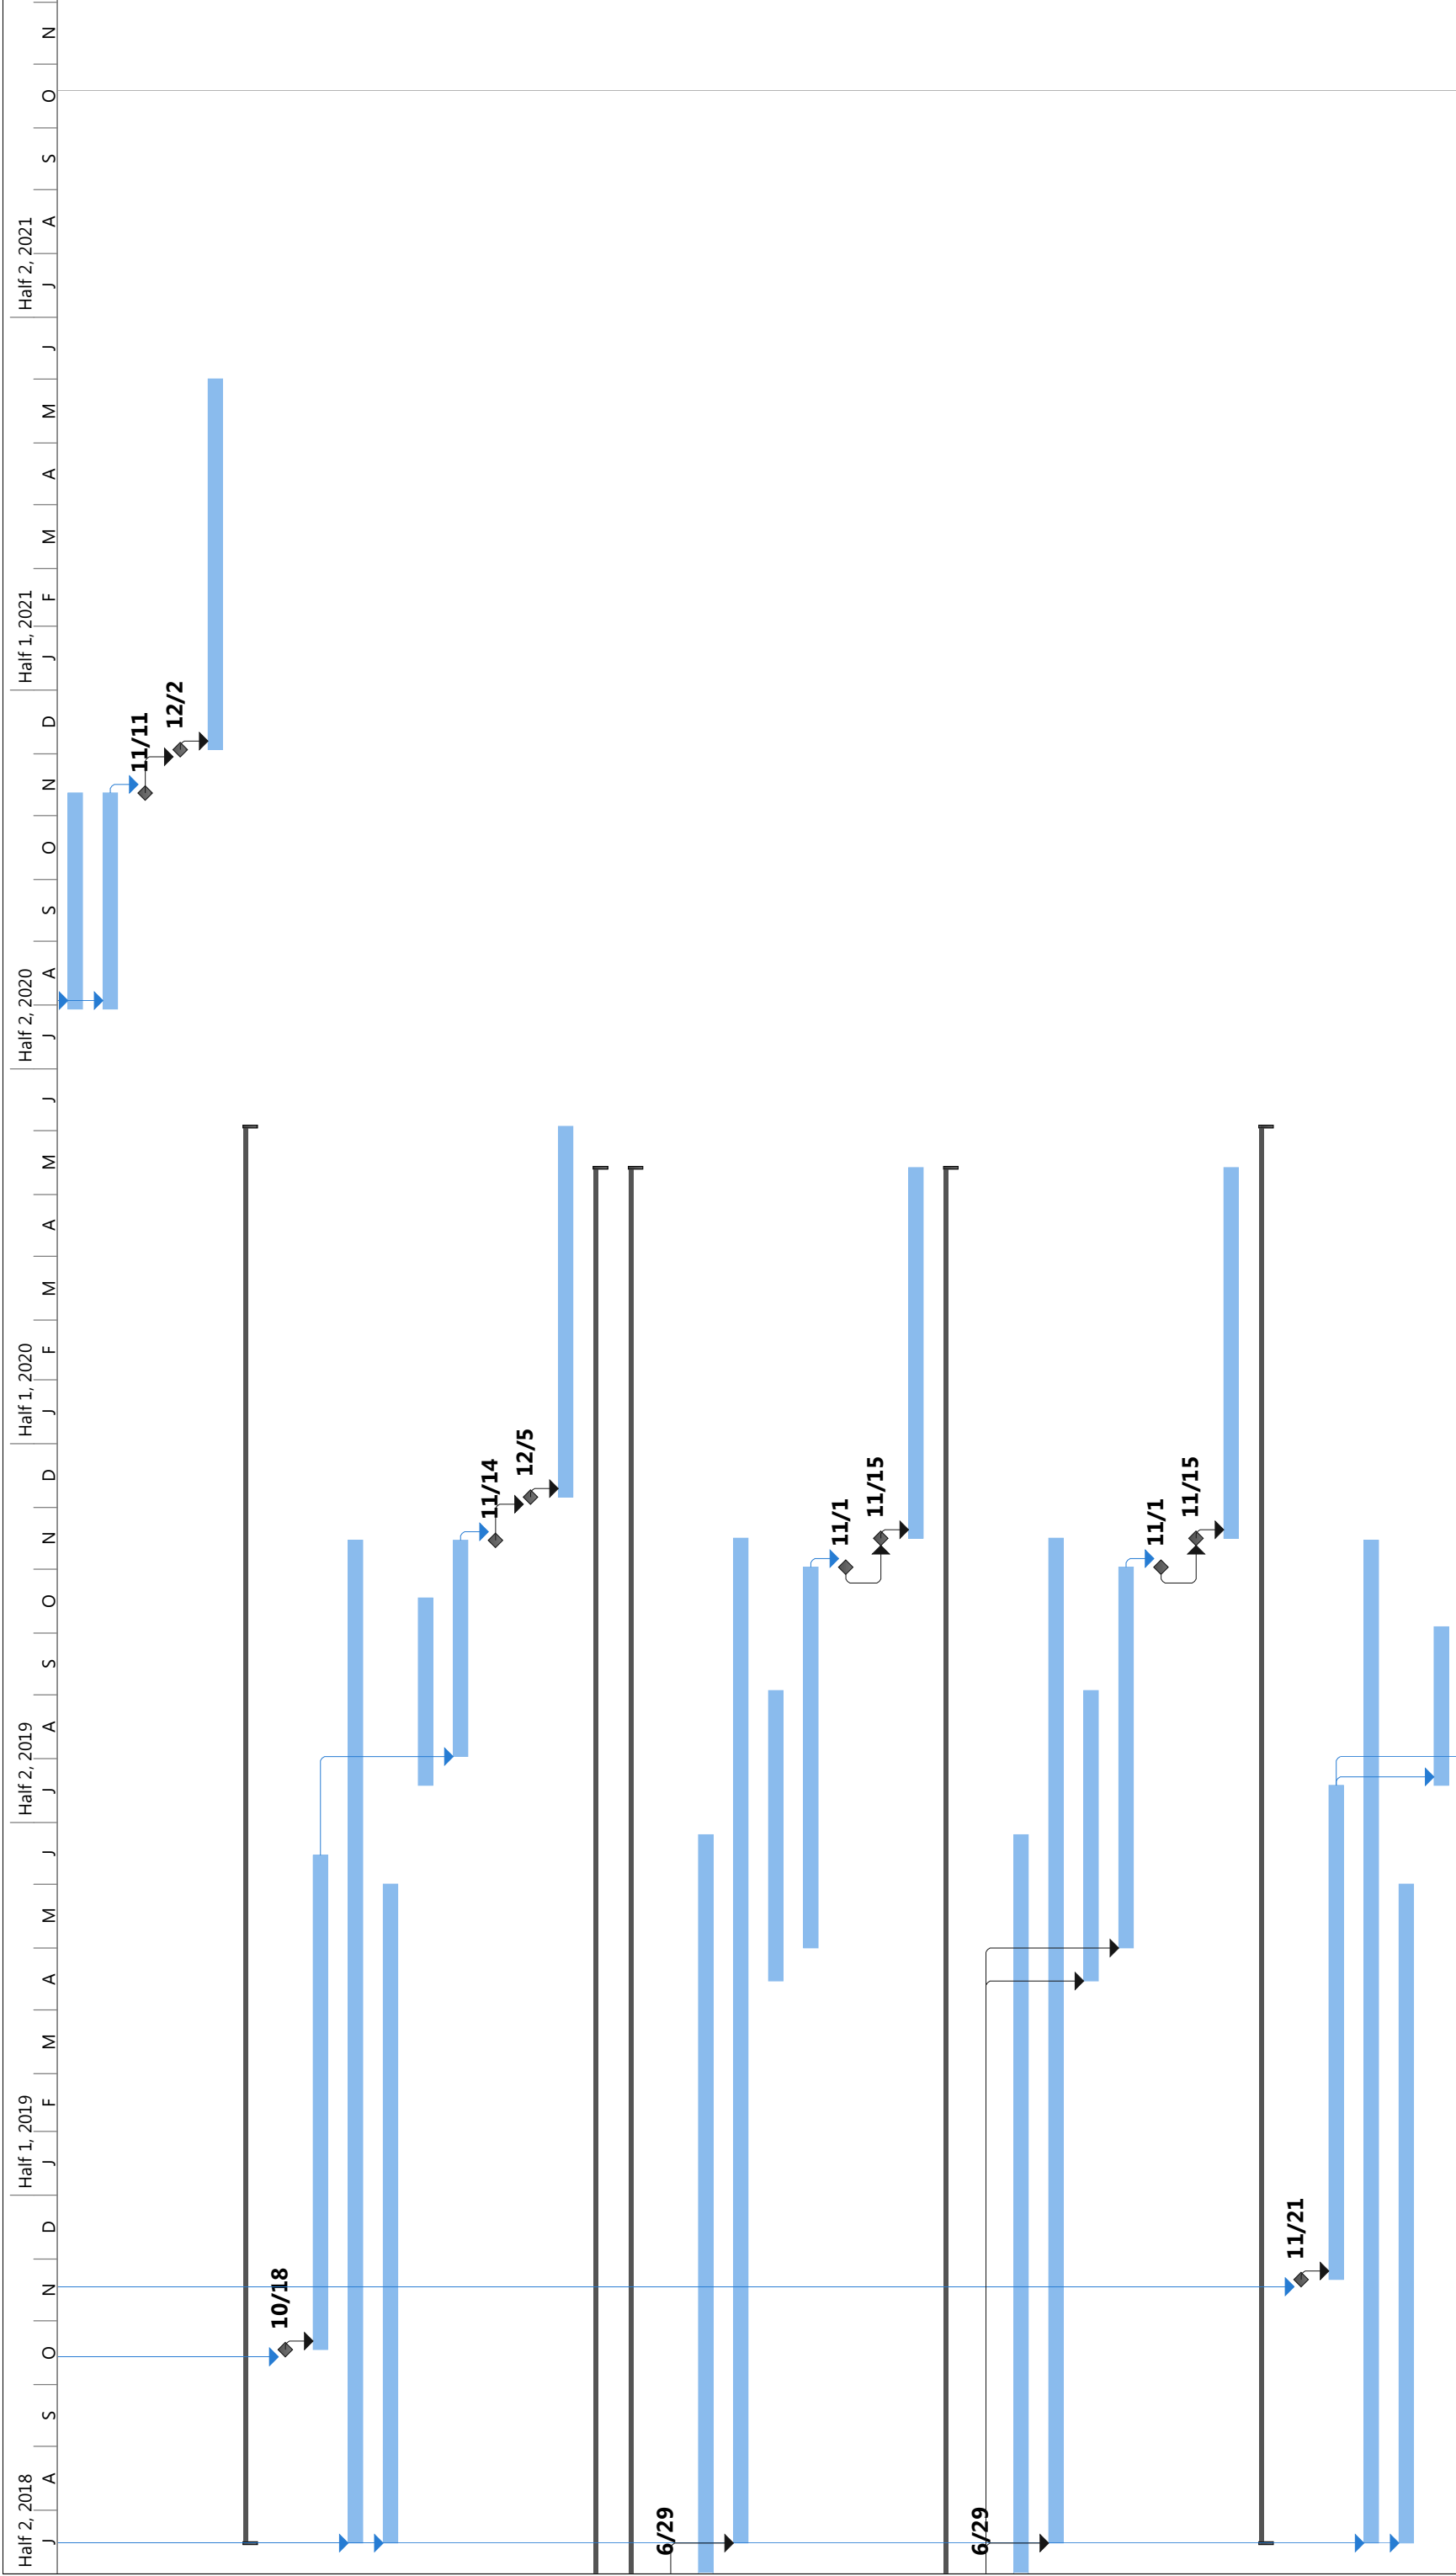

Project: Repower Schedule	Task	Split	Milestone	Summary	Project Summary
Date: Fri 1/26/18					

